Fireplace Specification Submission Form

Custom Fireplace Order Request

MONTIGO

Cross off one box only ☒ from every applicable category

Fireplace Series

		Viewing Glass Length	Configuration	
Linear Burner 'C-View'		3' to 24'	**Single Sided**	☐
3' to 6' long - 18" High Glass 7' to 24' long - 20" High Glass		3' to 24'	**See Thru**	☐
		3' to 24'	**Corner Left**	☐
		3' to 24'	**Corner Right**	☐
		5' to 24'	**Panorama**	☐
		3' to 9'	**Peninsula**	☐
Ventless, Linear Burner	**'ODD'** Outdoor	5' to 12'	**Single Sided**	☐
5' to 6' long - 18" High Glass 7' to 12' long - 20" High Glass	**'STIO'** Indoor/Outdoor	5' to 12'	**See Thru**	☐
Traditional Log Set 'BF'			**Single Sided**	☐
Standard Viewing Glass Size, Length X Height: 36" x 28", 52" x 36", 60" x 48", 84" x 48"			**See Thru**	☐
4-Sided, Linear Burner 'C4W'		3' to 16'	**with Posts**	☐
Minimum 30" Wide		3' to 16'	**Postless**	☐

Viewing Glass Size:
* See above Standard size listings

Fireplace Glass:
- Open Concept (No Glass) ☐
- Passive Cool Pack Glass ☐
- Powered Cool Pack Glass ☐

Power Vent Location:
- Inline ☐
- Wall ☐
- Roof ☐

Gas Inlet Location:
* For Indoor/Outdoor, this is the location when facing the Indoor Glass.
- Left Side ☐
- Right Side ☐
- Other ☐

Gas Type:
- Natural Gas ☐
- Liquid Propane Gas ☐

Flame Pattern:
* Only option & only Available on BF Series.
- 8" Tall Flame, Concealed Burner ☐
- 18" Tall High/Low Flame, Concealed Burner ☐
- * Traditional Log Set Burner ☐

FireStone Media:
* MUST BE placed over all Concealed Burners.
Not required for BF Series.
- Standard White/Silver/Opaque FireStone ☐
- Standard Ebony FireStone ☐
- Alternate FireStone (Additional Cost) ☐

Additional Optional Media:
- FireGlass ☐
- River Rock ☐

OK to Split Glass Panes:
Pane not split for C-View units up to 8' long.
Unless noted, Pane is split for C-View units, 9' to 12' long.
Pane is always split for C-View units 13' long and above.
- Yes ☐
- No ☐

PROJECT NAME

LOCATION

APPLICATION: **Public** ☐ | **Residential** ☐

SPECIAL REQUIREMENTS

COMPANY NAME

CONTACT NAME

DATE / / (MM / DD / YY)

Power Vent Pre-Ship: ☐ ← **To Request Pre-Ship, Cross off Pre-Ship Box(es)**

Electrical Panel / Fireplace Cable: Length (Standard 30'): ☐

Optional Combustion Air Intake
- Inline Damper (No Intake Box Included) ☐
- Louvered Intake Box w/ Damper ☐
- Intake Box ONLY (No Damper) ☐
- Louvered Intake Box ONLY (No Damper) ☐

Damper Cable - Length (Standard 30'):

Optional Flue Gas Termination Components:
* Only for units with Inline Power Vent.
- Built-in Damper for Roof Mounted Power Vent ☐
- Inline Damper (Used with Inline or Wall Mount P.V.) ☐
- * Louvered Termination Box w/ Damper ☐
- * Termination Box ONLY (No Damper) ☐
- * Louvered Termination Box ONLY (No Damper) ☐

Damper Cable - Length (Standard 30'):

Optional Pressure Stack Vent for INLINE P.V.:
- **Pressure Stack Vent** - Qty:
- **Splice Kit** - Qty:

Optional Sound Reducer for OPEN CONCEPT (NO GLASS) Fireplace:
- Yes ☐
- No ☐

VERSION 10.2014

Combustion Air Supply Submission Form

Custom Fireplace Order Request

Rear Air Intake



Number of Elbows: (90° or 45°)		Will Intake Pipes be combined?	Yes ☐ No ☐
Total Vertical:		Total Horizontal:	

Measurement in Feet

Front Air Intake



NOTE: This option is NOT available on Peninsula units.

Number of Elbows: (90° or 45°)		Will Intake Pipes be combined?	Yes ☐ No ☐
Total Vertical:		Total Horizontal:	

Measurement in Feet

Bottom Air Intake



Number of Elbows: (90° or 45°)		Will Intake Pipes be combined?	Yes ☐ No ☐
Total Vertical:		Total Horizontal:	

Measurement in Feet

Top Air Intake



NOTE: This option is ONLY available on Peninsula units.

Number of Elbows: (90° or 45°)		Will Intake Pipes be combined?	Yes ☐ No ☐
Total Vertical:		Total Horizontal:	

Measurement in Feet

One Side Left Air Intake



One Side Right Air Intake



NOTE:
These options are NOT available on any configurations greater than 8 feet, or on Panorama or Peninsula units.

Number of Elbows: (90° or 45°)		Will Intake Pipes be combined?	Yes ☐ No ☐
Total Vertical:		Total Horizontal:	

Measurement in Feet

Side Air Intake



NOTE: This option is NOT available on Panorama or Peninsula units.

Number of Elbows: (90° or 45°)		Will Intake Pipes be combined?	Yes ☐ No ☐
Total Vertical:		Total Horizontal:	

Measurement in Feet

VERSION 10.2014

Flue Vent Configuration Submission Form

Custom Fireplace Order Request

Horizontal Termination

"SBFPV" Wall Mount Power Vent

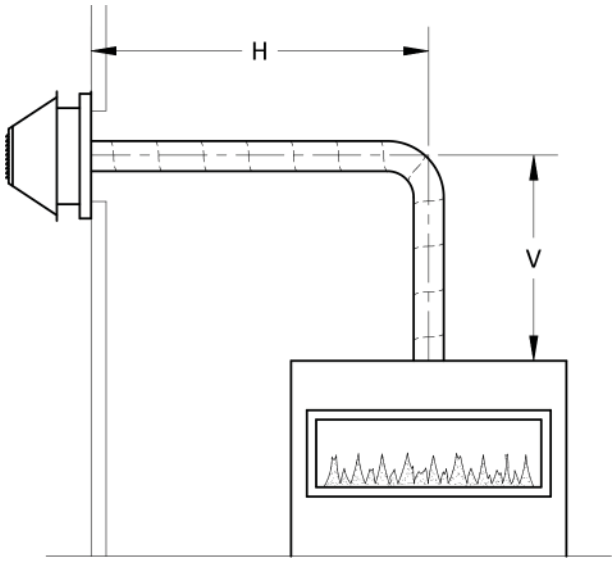

Number of Elbows (90° or 45°):			
Total Vertical 'V':		Total Horizontal 'H':	

Measurement in Feet

Vertical Termination

"SBFPV" Roof Mount or "BFUDPV" Updraft Roof Mount Power Vent

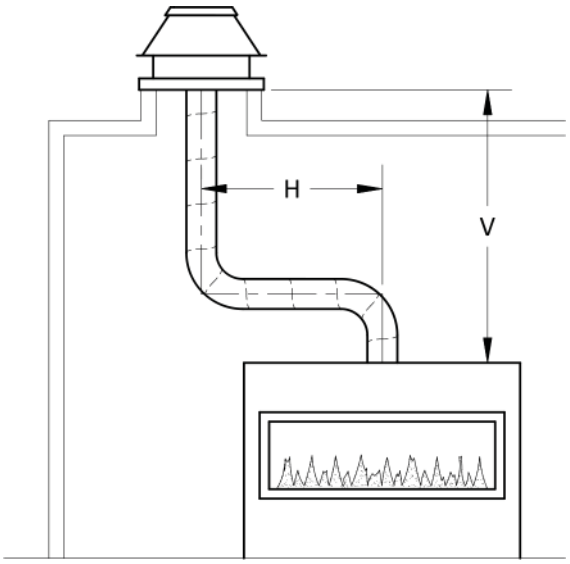

Number of Elbows (90° or 45°):			
Total Vertical 'V':		Total Horizontal 'H':	

Measurement in Feet

Inline Termination

"INPV-BF" Inline Power Vent

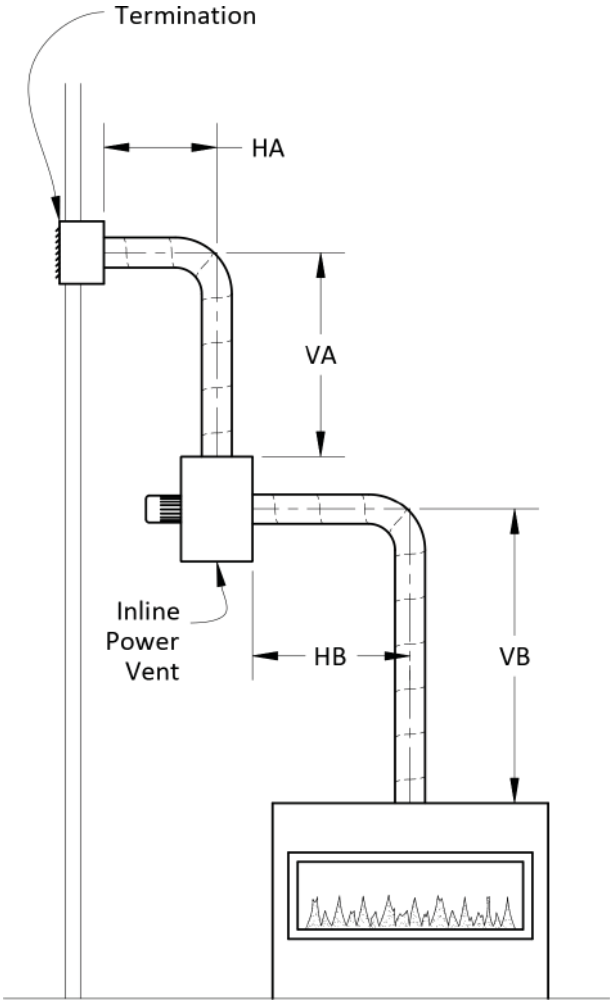

Number of Elbows (90° or 45°):	
Total Vertical, After Power Vent 'VA':	
Total Horizontal, After Power Vent 'HA':	
Total Vertical, Before Power Vent 'VB':	
Total Horizontal, Before Power Vent 'HB':	

Measurement in Feet

VERSION 10.2014
